

ADDENDUM 1, February 14, 2023

**RE: Paradise Unified School District
Pine Ridge Elementary School
Furniture RFP
Studio W Project Number 19033.199.34**

**From: Studio W Architects
1930 H Street, Sacramento, CA 95811**

To: Prospective Bidders

This Addendum forms a part of the Contract Documents and modifies the original bidding documents as noted below. Acknowledge receipt of this Addendum in the space provided on the Bid Form. Failure to do so may subject Bidder to disqualification.

The following changes or clarifications shall be made part of the Bid Documents and shall be taken into consideration when submitting bids.

- A. The Stevens ID Mobile Flat Storage, model number 80382 E36 has been discontinued. The replacement is part number 80382 F36.

Pre-Bid Questions:

- 1. Q: Please confirm installation start date.
 - a. Removal of furniture and installation of new work can begin **June 12, 2023** with exception to the new administration building in construction now. Furniture installation for the administration building can begin when the building is substantially complete which is currently scheduled for **July 25, 2023**.
- 2. Q: Can you please forward the construction schedule for the separate modernization project happening concurrently?
 - a. Construction schedule attached for reference.

Attachments:

- 1. Construction schedule for separate modernization project.


END OF ADDENDUM 1

Distribution: PUSD
Studio W Project File 19033.199.34

Note: It is incumbent upon the Prime Bidder to notify his subcontractor and/or materials supplier of the above changes in the Contract Documents.

For: Pine Ridge Elementary School
Furniture RFP


Studio **W** Architects
1930 H Street, Sacramento, CA 95811
(916) 254-5600

A handwritten signature in blue ink, appearing to read 'Brian P. Whitmore', is written over a horizontal line. The signature is stylized and cursive.

Brian P. Whitmore, AIA

C30345

STATE OF CALIFORNIA – DIVISION OF THE STATE ARCHITECT

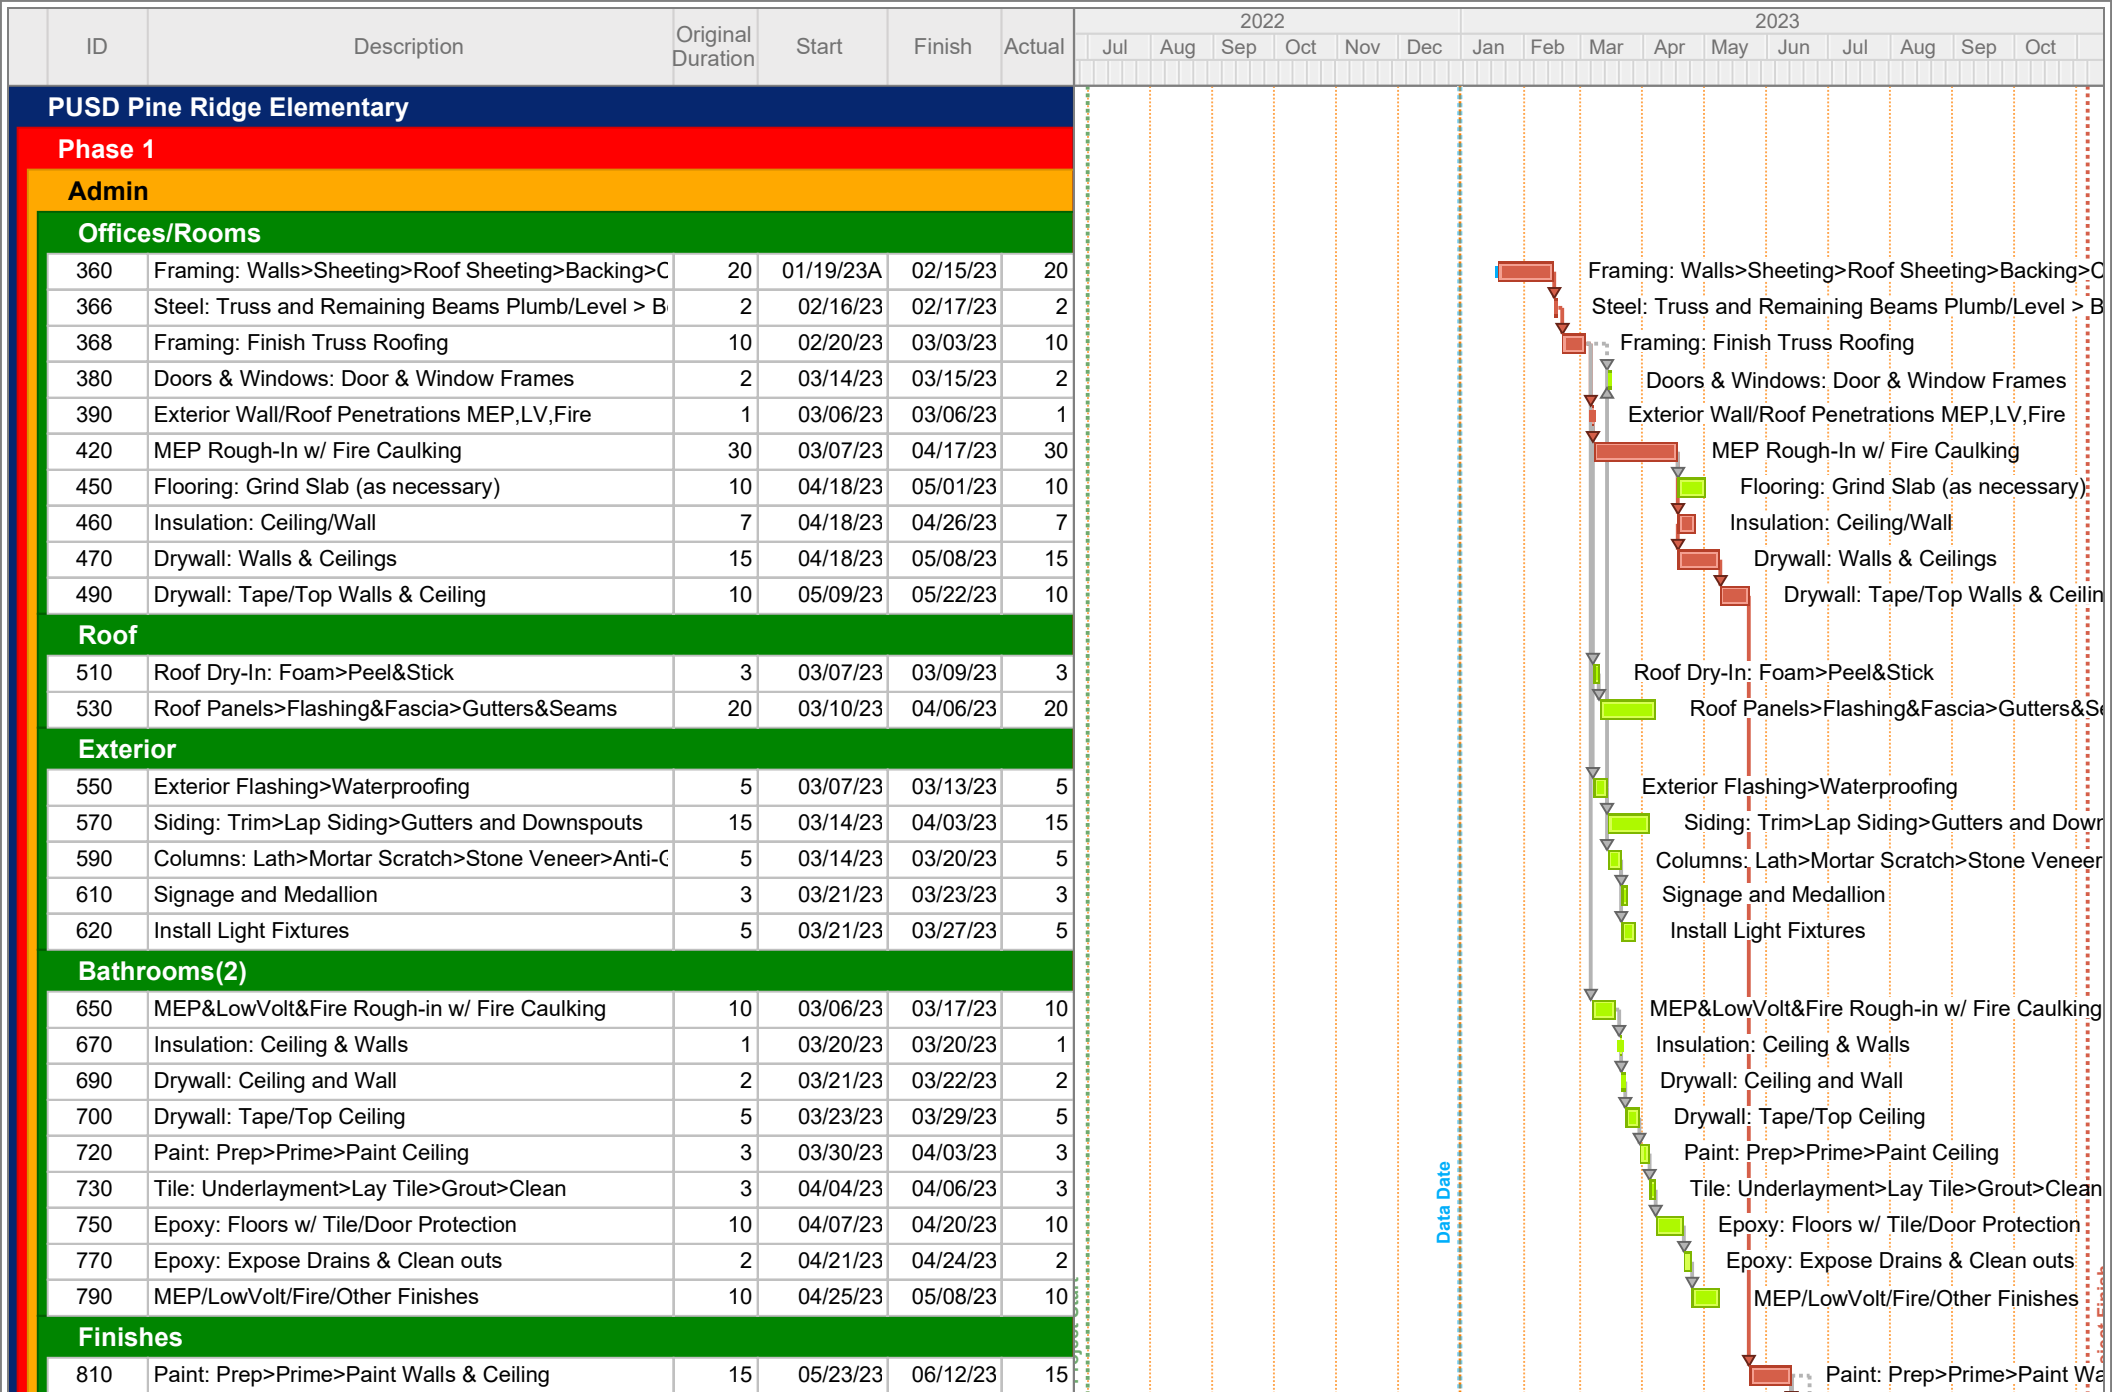


Run Date: 02/02/23

PUSD Pine Ridge Elementary
13878 Compton Drive, Magalia CA 95954



ID	Description	Original Duration	Start	Finish	Actual
Bathrooms(4)					
2940	MEP&LowVolt&Fire Rough-in w/ Fire Caulking	3	06/15/23	06/19/23	3
2960	Insulation: Ceiling & Walls	1	06/20/23	06/20/23	1
2980	Drywall: Ceiling and Wall	2	06/21/23	06/22/23	2
2990	Drywall: Tape/Top Ceiling	5	06/23/23	06/29/23	5
3010	Paint: Prep>Prime>Paint Ceiling	3	06/30/23	07/04/23	3
3020	Tile: Underlayment>Lay Tile>Grout>Clean	3	07/05/23	07/07/23	3
3040	Epoxy: Floors w/ Tile/Door Protection	7	07/10/23	07/18/23	7
3060	Epoxy: Expose Drains & Clean outs	2	07/19/23	07/20/23	2
3080	MEP/LowVolt/Fire/Other Finishes	5	07/21/23	07/27/23	5
Finishes					
3100	Paint: Prep>Prime>Paint Walls & Ceiling	3	07/04/23	07/06/23	3
3120	Install Ceiling Grid	1	07/07/23	07/07/23	1
3130	MEP&LowVolt Ceiling Device Drops	1	07/10/23	07/10/23	1
3150	Drop Ceiling Tiles	3	07/11/23	07/13/23	3
3160	Fire Extinguisher Cabinets	1	07/07/23	07/07/23	1
3170	Interior Signage	1	07/07/23	07/07/23	1
3180	Roller Window Shades	1	07/07/23	07/07/23	1
3190	MEP&LowVolt Device Trim out	3	07/07/23	07/11/23	3
3200	Floor Prep	1	07/07/23	07/07/23	1
3210	Flooring & Base	2	07/10/23	07/11/23	2
3220	Corner Guards	1	07/12/23	07/12/23	1
3250	Restoration, Clean & Punch	2	07/28/23	07/31/23	2
MPR					
MPR Room & Other(3)					
3280	Safe Off/Disconnect: MEP/LowVolt/Fire	1	05/26/23	05/26/23	1
3290	Layout: Demo	1	05/29/23	05/29/23	1
3300	Abatement & Soft Demo	2	05/29/23	05/30/23	2
3310	Layout: Hard/load bearing Demo	1	05/31/23	05/31/23	1
3320	Interior Hard/load bearing Demo	2	05/31/23	06/01/23	2
3350	Under slab Utilities	3	06/02/23	06/06/23	3
3370	Slab Patchback Pour	2	06/07/23	06/08/23	2
3390	Framing: HDRS, SFTS, CLG, Roof	3	06/02/23	06/06/23	3
3410	Coordination Meeting: All trades Backing	1	06/07/23	06/07/23	1
3420	Framing: Install Backing	1	06/07/23	06/07/23	1
3430	Doors & Windows: Door Frames	1	06/07/23	06/07/23	1

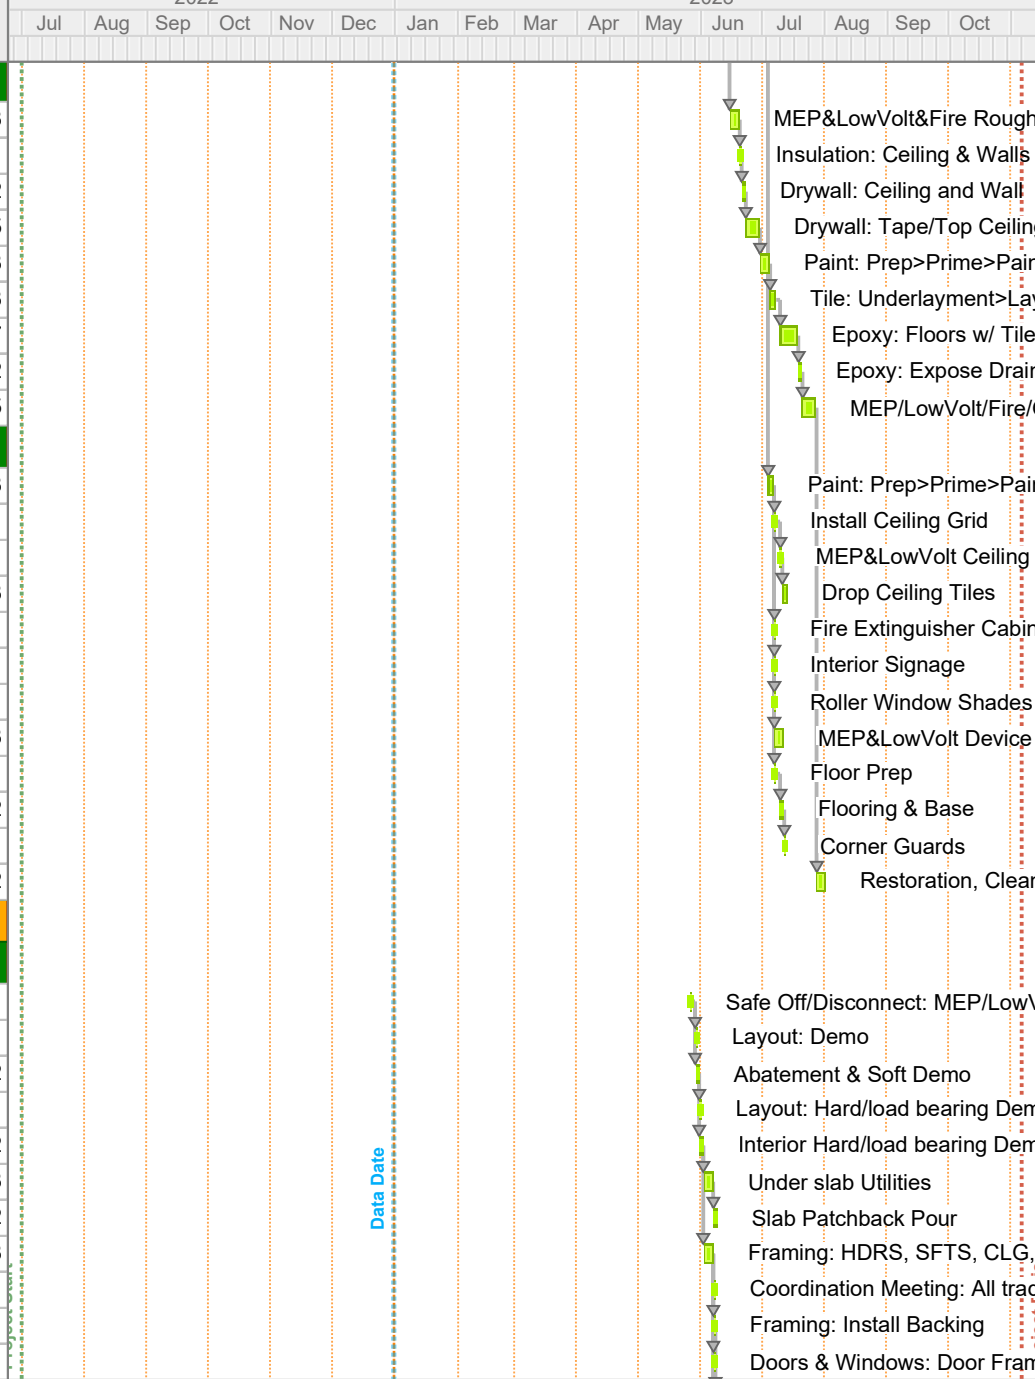

Run Date: 02/02/23

PUSD Pine Ridge Elementary
13878 Compton Drive, Magalia CA 95954



